



## TOWN OF REDINGTON SHORES, FLORIDA

Debris Management Daily Report

OCTOBER 13, 2024

HURRICANE HELENE | FEMA DR-4828

83°

TODAY'S WEATHER

1,468.8 CY

TODAY'S VOLUME

80

TODAY'S LOADS

2

DAY OF OPERATIONS

### DAILY ACTIVITY SUMMARY

2024 Hurricane Helene debris removal operations commenced at 0700 in the town of Redington Shores, FL today. Representatives from Rostan and Phillips & Jordan mustered prior to commencing field operations to outline the daily operating plan and discuss health and safety best practices.

Phillips & Jordan utilized 16 hauling units throughout the day to remove and properly dispose of hurricane debris from designated Rights-of-Way (ROWs). Debris removal operations continued until 1900.

There were no incidents to report.



### DEBRIS REMOVAL CREWS

Phillips & Jordan utilized 16 certified hauling units to remove hurricane debris from eligible ROWs. Removal efforts consisted solely of construction & demolition (C&D) debris.

### MONITORING

Rostan personnel were assigned to monitor and document work performed by Phillips & Jordan crews along designated ROWs and to verify disposal at Toytown DMS. Staffing levels were determined based on the anticipated work plan.

### AREAS WORKED



Phillips & Jordan crews cleared hurricane debris from along:

182<sup>nd</sup> Avenue East

180<sup>th</sup> Avenue East

## OCTOBER 14, 2024 — OPERATIONS PLAN


Debris Removal Operations will commence at approximately 0700 and conclude at or near 1900. Phillips & Jordan crews will muster with Rostan personnel prior to departing for the field.

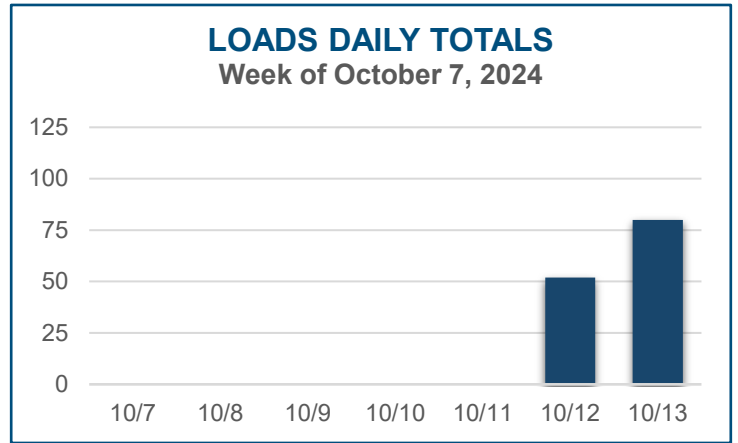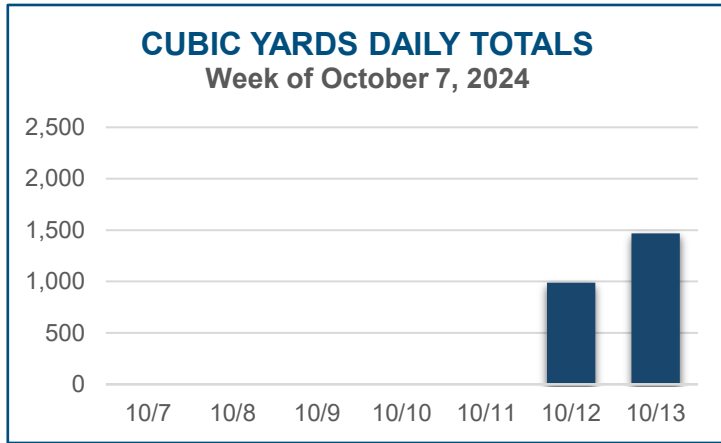

## DEBRIS REMOVAL SUMMARY: CONSTRUCTION & DEMOLITION (C&D)

DISPOSAL SITE	LOADS TODAY	LOADS TOTAL	DEBRIS ACCEPTED TODAY [CUBIC YARDS]	DEBRIS ACCEPTED TOTAL [CUBIC YARDS]
TOYTOWN DMS	80	132	1,468.80	2,457.20
<b>PROJECT TOTALS – C&amp;D</b>	<b>80</b>	<b>132</b>	<b>1,468.80</b>	<b>2,457.20</b>

## DEBRIS LOADING LOCATIONS – OCTOBER 13, 2024

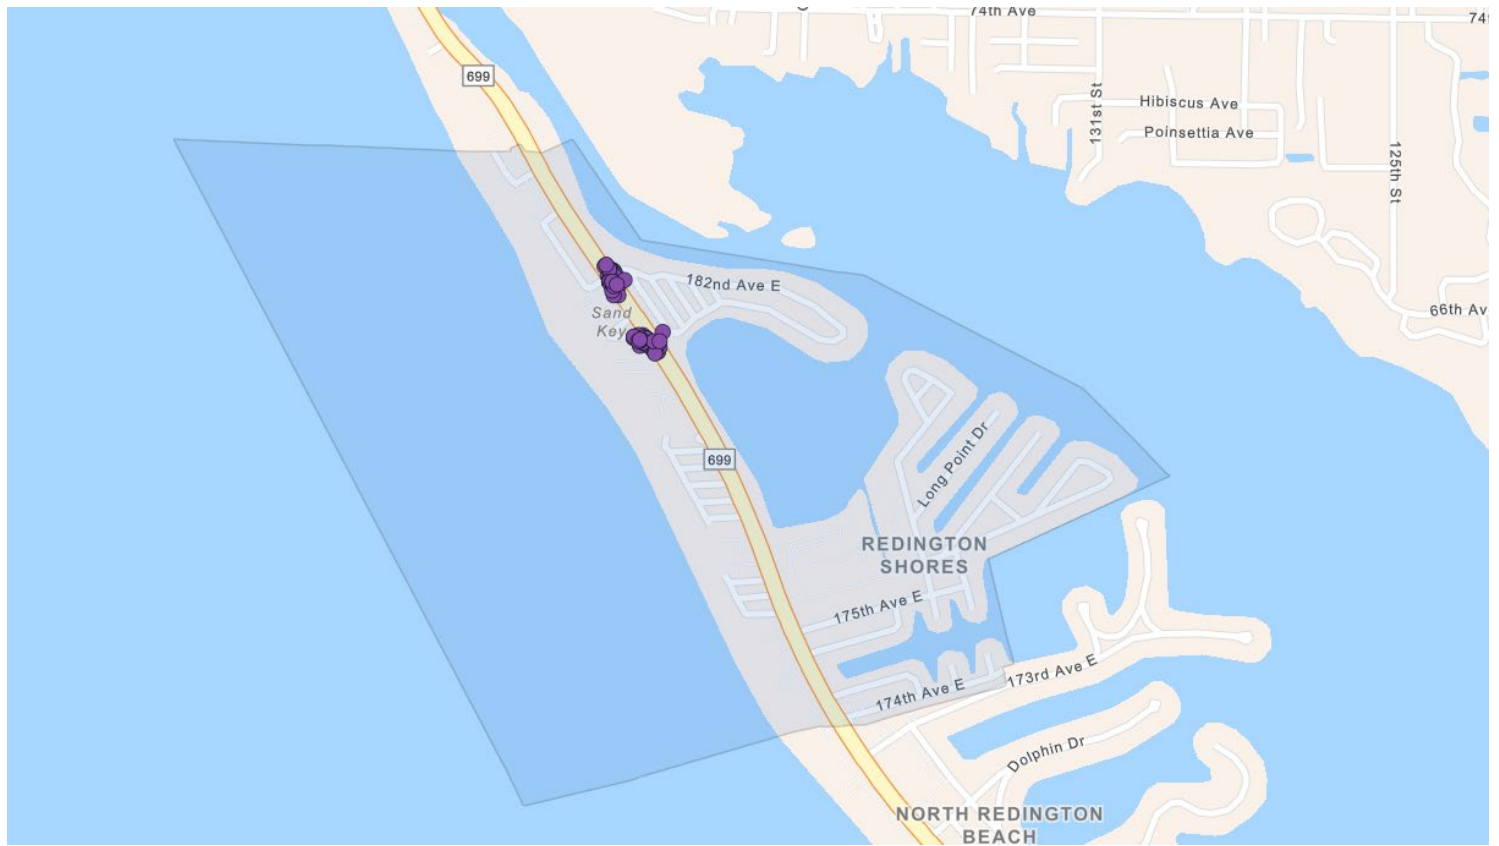

## DEBRIS LOADING LOCATIONS TO DATE

